02

PM KNOWLEDGE AREAS

Bidang Pengetahuan Manajemen Proyek

Copyright © March 2026

Project Management Knowledge Areas

- PMI menciptakan seperangkat terminologi standar dan pedoman untuk manajemen proyek, yang dikenal sebagai bidang pengetahuan manajemen proyek. Ini adalah standar yang berkembang yang diperbarui secara berkala di PMBOK-nya.
- Bidang pengetahuan (**knowldege area**) manajemen proyek bertepatan dengan kelompok proses (**process group**), yang merupakan inisiasi proyek, perencanaan proyek, pelaksanaan proyek, pemantauan dan pengendalian, dan penutupan proyek. Ini adalah fase kronologis yang dilalui setiap proyek.
- Kita dapat menganggap kelompok proses sebagai horizontal, sedangkan bidang pengetahuan vertikal. Bidang pengetahuan adalah materi pokok teknis inti, yang diperlukan untuk manajemen proyek yang efektif.

Copyright © March 2026

5 Pocess Groups and 10 Knowledge Area

5 Process Groups
Initiating Process Group
Planning Process Group
Executing Process Group
Monitoring & Controlling Process Group
Closing Process Group

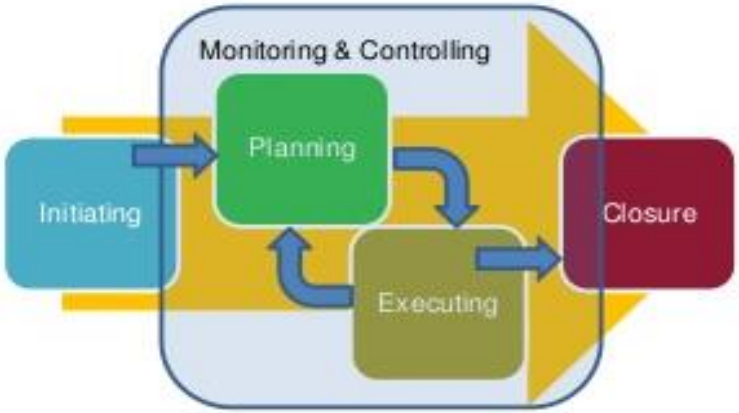

10 Knowledge Areas
Integration Management
Scope Management
Time Management
Cost Management
Quality Management
Human Resource Management
Communication Management
Risk Management
Procurement Management
Stakeholder Management

www.GLOBALSKILLUP.com

Copyright © March 2026

GAMBARAN KELOMPOK PROSES

Initiating
Process: **Develop project charter**
Output: Project charter

Planning
Process: **Develop project management plan**
Output: Project management plan

Executing
Process: **Direct and manage project work**
Outputs: Deliverables, work performance data, change requests, project management plan updates, project documents updates

Monitoring and Controlling
Process: **Monitor and control project work**
Outputs: Change requests, project management plan updates, project documents updates
Process: **Perform integrated change control**
Outputs: Approved change requests, change log, project management plan updates, project documents updates

Closing
Process: **Close project or phase**
Outputs: Final product, service, or result transition; organizational process assets updates

Project Start → **Project Finish**

Schwalbe, 2012

Copyright © March 2026

10 BIDANG PENGETAHUAN

Bidang pengetahuan adalah kopetensi utama yang harus dikembangkan seorang manajer proyek

- Empat bidang pengetahuan ini mengarah kepada proyek spesifik (lingkup, waktu, biaya dan mutu)
- Empat bidang pengetahuan yang merupakan alat pencapaian tujuan proyek (SDM, komunikasi, resiko, dan manajemen pengadaan)
- Satu bidang pengetahuan (manajemen integrasi proyek) mempengaruhi oleh semua bidang pengetahuan lainnya
- project integration management mempengaruhi dan dipengaruhi oleh 9 area pengetahuan lainnya

Copyright © March 2026

47 Proces PMBOK Process

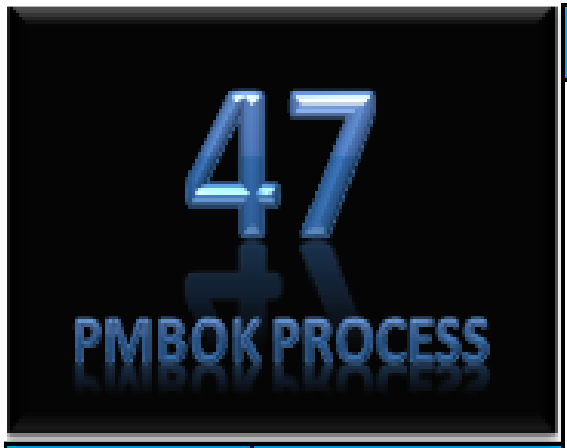

Phases	Groups	Knowledge Areas: Integration	Scope	Time	Cost	Quality	Human Resources	Communication	Risk	Procurement	Stakeholder		
Initiation	Initiating	1									1	2	→ 2 Areas
Panning	Planning	1	4	6	3	1	1	1	5	1	1	24	→ 10 Areas
Execution	Executing	1				1	3	1		1	1	8	→ 6 Areas
	Mon & Contr.	2	2	1	1	1		1	1	1	1	11	→ 9 Areas
Close-out	Closing	1								1		2	→ 2 Areas
		6	6	7	4	3	4	3	6	4	4	47	

source : https://www.youtube.com/watch?v=zYgf9OVUhnI

Copyright © March 2026

6 PROCESS	Knowledge Area
	1. INTEGRATION
Initialing	1.1 Develop Project Charter
Planning	1.2 Develop Project Management Plan
Executing	1.3 Direct and Manage Project Work
Monitoring and Controlling	1.4 Monitor and control Project Work
	1.5 Perform integrated Change Control
Closing	1.6 Close Project or Phase

1. Manajemen Integrasi Proyek

- **1.1. Mengembangkan Piagam Proyek.**
- **1.2. Mengembangkan Rencana Manajemen Proyek.**
- **1.3. Arahkan dan Kelola Pekerjaan Proyek**
- **1.4. Memantau dan Mengontrol Pekerjaan Proyek**
- **1.5. Lakukan Kontrol Perubahan terintegrasi**
- **1.6. Tutup Proyek atau Fase**

Copyright © March 2026

4 PROCESS	Knowledge Area
	2. SCOPE
Initialing	
Planning	2.1 Plan Scope Management
	2.2 Collect Requirements
	2.3 Define Scope
	2.4 Create WBS
Executing	
Monitoring and Controlling	2.5 Validate Scope
	2.6 Control Scope
Closing	

2. Manajemen Ruang Lingkup Proyek

2.1. Manajemen Lingkup Rencana
2.2. Kumpulkan Persyaratan
2.3. Tentukan Ruang Lingkup
2.4. Buat WBS.
2.5. Validasi Lingkup.
2.6. Kontrol Lingkup

Copyright © March 2026

7 PROCESS	Knowledge Area
	3. TIME
Initialing	
Planning	3.1 Plan Schedule Management
	3.2 Define Activities
	3.3 Sequence Activities
	3.4 Estimate Activity Resources
	3.5 Estimate Activities Durations
	3.6 Develop Schedule
Executing	
Monitoring and Controlling	3.7 Control Schedule
Closing	

3. Manajemen Waktu Proyek

3.1 Manajemen Jadwal Rencana
3.2 Menentukan Aktivitas
3.3 Urutan Aktivitas
3.4 Estimasi Sumber Daya Kegiatan
3.5 Perkiraan Durasi Kegiatan
3.6 Menyusun Jadwal
3.7 Jadwal Kontrol

Copyright © March 2026

4 PROCESS	Knowledge Area
	4. COST
Planning	4.1 Plan Cost Management
	4.2 Estimate Costs
	4.3 Determine Budget
Monitoring and Controlling	4.4 Control Cost

4. Manajemen Biaya Proyek

4.1. Rencanakan Manajemen Biaya.

4.2. Perkirakan Biaya.

4.3. Tentukan Anggaran.

4.4. Kontrol Biaya

Copyright © March 2026

3 PROCESS	Knowledge Area
	5. QUALITY
Initialing	
Planning	5.1 Plan Quality Management
Executing	5.2 Perform Quality Assurance
Monitoring and Controlling	5.3 Control Quality
Closing	

5. Manajemen Kualitas Proyek

5.1. Rencanakan Manajemen Mutu

5.2. Lakukan Penjaminan Mutu

5.3. Kualitas Kontrol

Copyright © March 2026

4 PROCESS	Knowledge Area
	6. HUMAN RESOURCES
Planning	6.1 Plan Human Resource Management
Executing	6.2 Acquire Project Team
	6.3 Develop Project Team
	6.4 Manage Project Team

6. Manajemen Sumber Daya Manusia

6.1. Rencanakan Manajemen SDM

6.2. Acquire Project Team.

6.3. Membentuk Team Project

6.4. Mengelola Team Project

Copyright © March 2026

3 PROCESS	Knowledge Area
	7. COMMUNICATIONS
Initialing	
Planning	7.1 Plan Communication Management
Executing	7.2 Manage Communication
Monitoring and Controlling	7.3 Control Communication
Closing	

7. Manajemen Komunikasi Proyek.

7.1. Manajemen Rencana Komunikasi.

7.2. Kelola Komunikasi.

7.3 Kontrol Komunikasi

Copyright © March 2026

6 PROCESS	Knowledge Area
	8. RISK
Planning	8.1 Plan Risk Management
	8.2 Identify Risks
	8.3 Perform Qualitative Risk analysis
	8.4 Perform Quantitative Risk
	8.5 Plan Risk Progress
Monitoring and Controlling	8.6 Control Risks

8. Manajemen Risiko Proyek

- **8.1. Rencanakan Manajemen Risiko.**
- **8.2. Identifikasi Risiko.**
- **8.3. Analisis Risiko Kualitatif**
- **8.4. Risiko Kuantitatif.**
- **8.5. Rencanakan Kemajuan Risiko.**
- **8.6. Kontrol Risiko.**

Copyright © March 2026

KATEGORI RISIKO

merencanakan dan mengelola ketidakpastian yang berdampak pada proyek

Kategori	Penjelasan Kategori Resiko
Manajemen Proyek	Risiko yang terkait dengan manajemen proyek misalnya kurang dukungan dari pihak manajemen, proses manajemen, proyek tidak memadai, ruang lingkup dan deliverable proyek tidak jelas.
Teknologi	Risiko yang terkait dengan desain dan implementasi proyek yang bersifat teknis, misalnya adopsi teknologi baru yang tidak sesuai dengan platform lama sehingga memunculkan bugs
Sumber daya	Risiko yang terkait dengan sumber daya proyek, misalnya pendanaan, ketersediaan personil yang memenuhi kualifikasi, ketersediaan sarana & prasarana, alokasi sumber daya.
Organisasi	Risiko yang terkait dengan isu internal organisasi, misalnya konflik kepemilikan proyek, perubahan kebijakan perusahaan.
Eksternal	Risiko yang terkait dengan faktor eksternal diluar proyek dan organisasi, misalnya faktor alam, perubahan regulasi pemerintah, isu ketenagakerjaan, krisis moneter.

Copyright © March 2026

4 PROCESS	Knowledge Area
	9. PROCUREMENT
Planning	9.1 Plan Procurement Management
Executing	9.2 Conduct Procurement
Monitoring and Controlling	9.3 Control Procurement
Closing	9.4 Close Procurement

9. Manajemen Pengadaan Proyek

9.1. Rencanakan Manajemen Pengadaan.

9.2. Melakukan Pengadaan.

9.3. Pengadaan Kontrol.

9.4. Tutup Pengadaan.

Copyright © March 2026

4 PROCESS	Knowledge Area
	10. STAKEHOLDER
Initialing	10.1 Identify Stakeholders
Planning	10.2 Plan Stakeholder Management
Executing	10.3 Manage Stakeholder Engagement
Monitoring and Controlling	10.4 Control Stakeholder Engagement

10. Manajemen Pemangku Kepentingan Proyek

10.1. Identifikasi Pemangku Kepentingan.

10.2. Manajemen Pemangku Kepentingan Rencana.

10.3. Kelola Keterlibatan Pemangku Kepentingan.

10.4. Mengontrol Keterlibatan Pemangku Kepentingan.

Copyright © March 2026

ITTOs PROJECT INTEGRATION MANAGEMENT

Project Integration Management Overview

4.1 Develop Project Charter

.1 Inputs
- .1 Project statement of work
- .2 Business case
- .3 Agreements
- .4 Enterprise environmental factors
- .5 Organizational process assets

.2 Tools & Techniques
- .1 Expert judgment
- .2 Facilitation techniques

.3 Outputs
- .1 Project charter

4.2 Develop Project Management Plan

.1 Inputs
- .1 Project charter
- .2 Outputs from other processes
- .3 Enterprise environmental factors
- .4 Organizational process assets

.2 Tools & Techniques
- .1 Expert judgment
- .2 Facilitation techniques

.3 Outputs
- .1 Project management plan

4.3 Direct and Manage Project Work

.1 Inputs
- .1 Project management plan
- .2 Approved change requests
- .3 Enterprise environmental factors
- .4 Organizational process assets

.2 Tools & Techniques
- .1 Expert judgment
- .2 Project management information system
- .3 Meetings

.3 Outputs
- .1 Deliverables
- .2 Work performance data
- .3 Change requests
- .4 Project management plan updates
- .5 Project documents updates

4.4 Monitor and Control Project Work

.1 Inputs
- .1 Project management plan
- .2 Schedule forecasts
- .3 Cost forecasts
- .4 Validated changes
- .5 Work performance information
- .6 Enterprise environmental factors
- .7 Organizational process assets

.2 Tools & Techniques
- .1 Expert judgment
- .2 Analytical techniques
- .3 Project management information system
- .4 Meetings

.3 Outputs
- .1 Change requests
- .2 Work performance reports
- .3 Project management plan updates
- .4 Project documents updates

4.5 Perform Integrated Change Control

.1 Inputs
- .1 Project management plan
- .2 Work performance reports
- .3 Change requests
- .4 Enterprise environmental factors
- .5 Organizational process assets

.2 Tools & Techniques
- .1 Expert judgment
- .2 Meetings
- .3 Change control tools

.3 Outputs
- .1 Approved change requests
- .2 Change log
- .3 Project management plan updates
- .4 Project documents updates

4.6 Close Project or Phase

.1 Inputs
- .1 Project management plan
- .2 Accepted deliverables
- .3 Organizational process assets

.2 Tools & Techniques
- .1 Expert judgment
- .2 Analytical techniques
- .3 Meetings

.3 Outputs
- .1 Final product, service, or result transition
- .2 Organizational process assets updates

Copyright © March 2026

KEGIATAN PROJECT INTEGRATION MANAGEMENT

A. Melakukan identifikasi dokumen pengembangan proyek

1. Karakteristik dari jasa/produk ditetapkan.
2. Batasan batasan dan asumsi dokumen yang diperlukan dilakukan identifikasi.

B. Melakukan analisis studi kelayakan awal

1. Model keputusan dan metode pemilihan proyek termasuk metode pengukuran manfaat dan metode optimasi terbatas dipilih.
2. Informasi secara historis untuk proyek yang melibatkan kemiripan produk dan jasa dievaluasi.
3. Penilaian tingkat tinggi terhadap sumberdaya organisasi proyek dilakukan.
4. Penilaian tingkat tinggi terhadap persyaratan teknis dan nonteknis proyek dilakukan.

C. Mengembangkan project charter

1. Pernyataan pekerjaan proyek (Project statement of work)
2. Peralatan dan cara (Tools & Techniques)

Copyright © March 2026

KEGIATAN PROJECT INTEGRATION MANAGEMENT

D. Mengembangkan rencana manajemen proyek (Project Management Plan)

1. PM plan tamplate, prosedur perubahan, informasi proyek yang lalu diidentifikasi sebagai masukan proses selanjutnya.
2. fasilitas teknis digunakan untuk menghasilkan Rencana Pengelolaan Proyek (Project Management Plan)

E. Mengarahkan dan mengelola pekerjaan proyek

1. PMIS
2. deliverables

F. Memantau dan mengendalikan pekerjaan proyek

1. Rencana pengelolaan proyek (Project management plan)
2. permintaan perubahan, laporan kinerja pekerjaan

G. Melakukan pengendalian perubahan secara terintegrasi

H. Menyerahkan/menutup proyek

Copyright © March 2026

TUGAS MANDIRI [TM]-01			
PENUGASAN	**PERTEMUAN - 02**	PENGUMPULAN	**AWAL PERTEMUAN - 03**
KETENTUAN :			
1. GUNAKAKAN KERTAS A4			
2. DITULIS TANGAN / NON-KOMPUTER			
3. DIBERI NAMA, NIM, KELAS, NO.ABSEN			

Tugas menyusun Proces-Proces Group Proyek dengan mencetak, menggunting dan menempel sesuai dengan Kanvasnya.

Keterangan :

Materi bisa di download melalui web

ricardo_vargas_simplified_pmbok_flow_5ed_canvas_en

Copyright © March 2026

CATATAN PENGUAT MATERI KULIAH

Soal Latihan dan Soal ujian dapat dari sumber materi slide tiap pertemuan dan ditambah dari luar slide pertemuan (dari buku-buku referensi) maka Mahasiswa diharapkan membaca dan mencari materi tambahan yang masih terkait dengan topik pertemuan dari sumber referensi buku Manajemen Proyek Sistem Informasi untuk menambah wawasan keilmuan agar nantinya dapat menjawab soal-soal latihan maupun soal ujian yang sumbernya bukan berasal dari slide pertemuan.

Copyright © March 2026
